


Baton Rouge SSO Program

Progress Report



May 2011

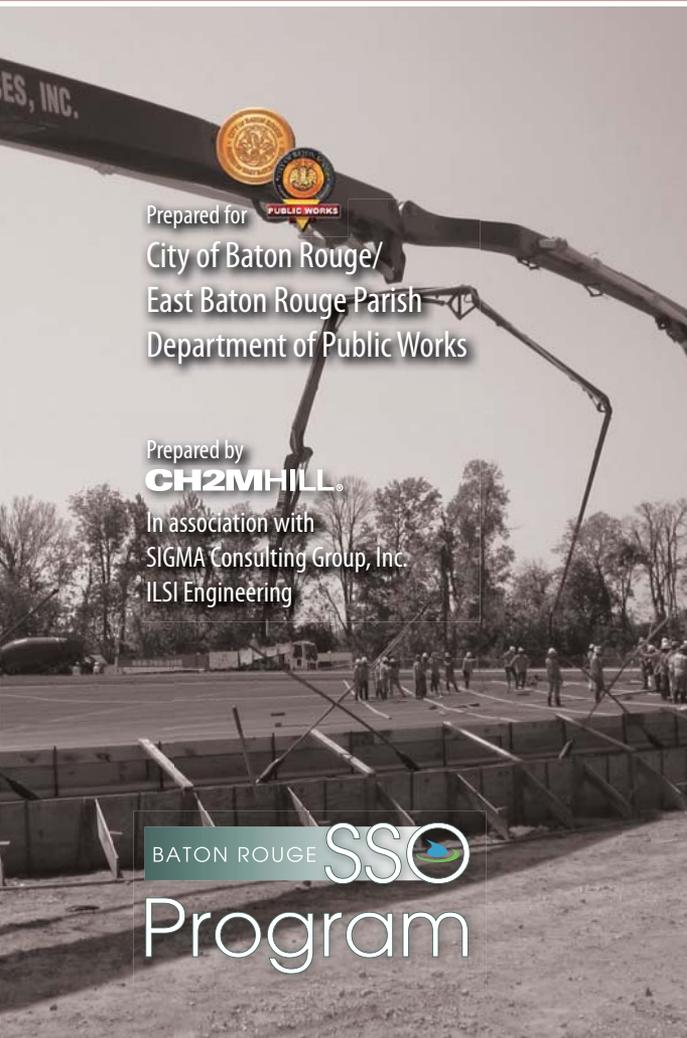



In the Spotlight...

Are you Red Stick Ready?

The SSO Program is partnering with the Mayor-President's Office and the Department of Public Works to improve the community's preparedness by participating in the Red Stick Ready Program.

East Baton Rouge Parish is a national leader in emergency readiness. Under the leadership of Mayor-President Melvin L. "Kip" Holden and the Mayor's Office of Homeland Security and Emergency Preparedness, the Parish has developed the Red Stick Ready program to provide information to residents to help them prepare for, respond to, and recover from any and all emergency situations.

This readiness campaign has been nationally recognized and contributed to the Parish achieving the designation of a Storm Ready Community by the National Weather Service. The Mayor's Office of Homeland Security and Emergency Preparedness has also achieved the highest national certification from the Emergency Management Accreditation Program.

With the beginning of hurricane season on June 1 and another summer of sweltering heat, we encourage you to contact the Office of Homeland Security and Emergency Preparedness and prepare for an emergency by creating an emergency plan, preparing disaster supply kits for your home and auto, learning the meanings of watch, warning, and protective action recommendations, and participating in the buddy system aiding elderly or infirmed neighbors and family. Preplanning for an emergency can reduce the possibility of personal injury, loss of life, and damage to property.


To find out how to be Red Stick Ready, contact 225-389-2100 or go to www.redstickready.com.

RED ST/CK R E A D Y

The SSO Program is improving the City-Parish's ability to manage storm events by:

- Adding 122 million gallons of storage capacity during heavy rain events
- Installing emergency generators at all Parish pump stations and two treatment plants
- Inspecting and repairing or replacing 1,042 miles of sewer pipeline
- Upgrading more than 66 miles of gravity sewer, 127 miles of forcemain, and 147 pump stations

Projects Under Construction

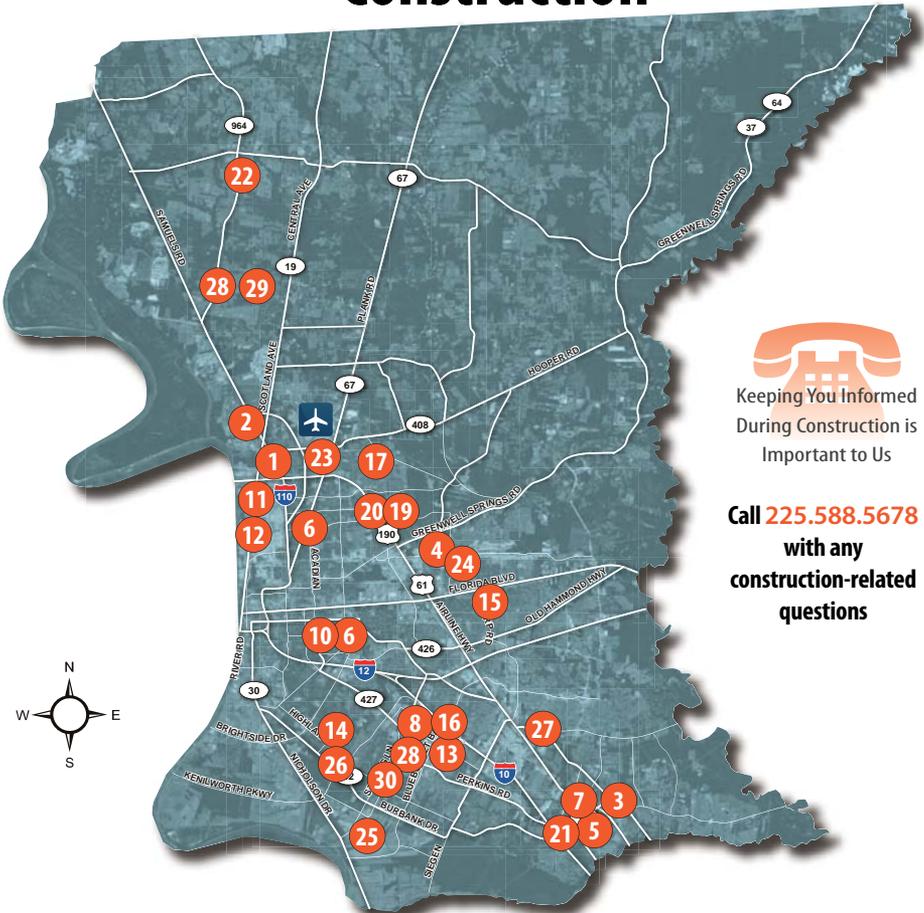

Keeping You Informed
During Construction is
Important to Us

Call 225.588.5678
with any
construction-related
questions

- | | | |
|--|--|--|
| <ul style="list-style-type: none"> 1 Elm Grove Garden Road – Harding Blvd 2 Scotland Avenue – Progress Road 3 Group Project 2 – Small Pump Stations 4 Oak Villa Blvd – Choctaw Street 5 Highland Road – Buchanan St 6 Foster Drive – Government Street (Phase A) 7 Nicholson Dr – Highland Rd – Perkins Rd (Phase A) 8 Citiplacé/Essen Area 9 South Blvd–St. Joseph St/25th St – N. Acadian Thruway 10 Foster Drive – Government St (Phase B) 11 Capitol Lake Dr – Gayosa St/25th St – N. Acadian Thruway | <ul style="list-style-type: none"> 12 Downtown Area – Pump Station Improvements 13 Bluebonnet Blvd – Jefferson Hwy Phase 1 14 Kenilworth Blvd – Boone Drive 15 Sharp Road – Florida Blvd 16 Bluebonnet Blvd – Jefferson Hwy Phase 2 17 Silverleaf Road – Ford Street 18 Multiple PS – Jefferson Hwy – Park Forest Drive 19 Brookstown Road – Evangeline Street (Phase 2) 20 Brookstown Road – Evangeline Street (Phase 1) 21 Highland Road – Burbank Drive 22 Zachary Area Transmission Network (Phase 4) | <ul style="list-style-type: none"> 23 Group Project 1A (Veterans Parkway – Gravity Mains) 24 Choctaw Storage and PS Facility 25 SWWTP Wet Weather Improvements (Phase 1) 26 Central Consolidation - PS42FM (Phase A) 27 Perkins/Old Perkins Area – Booster PSS14 28 Zachary Area Transmission Network (Phase 1) 29 Zachary Area Transmission Network (Phase 3) 30 Staring Lane FM (Ph 2 – Highland to Perkins) 31 Emergency Generators Purchasing* 32 Emergency Generators Installation* |
|--|--|--|

*Throughout the City – Parish



1. **Elm Grove Garden Road – Harding Blvd:** This rehabilitation project involves rehabilitating approximately 199,500 linear feet of gravity main and 839 manholes.
2. **Scotland Avenue – Progress Road:** This rehabilitation project involves inspecting and rehabilitating, as needed, approximately 208,000 linear feet of forcemain and 300 manholes.
3. **Group Project 2 – Small Pump Stations:** This capacity improvement project involves replacing seven pump stations that will work in conjunction with the forcemain upgrades in other South Forced Lower Basin projects.
4. **Oak Villa Blvd – Choctaw Street:** This rehabilitation project involves inspecting and rehabilitating, as needed, approximately 245,000 linear feet of forcemain and 990 manholes.
5. **Highland Road – Buchanan Street:** This capacity improvement project involves upgrading approximately 4,465 linear feet of forcemain and 8,390 linear feet of gravity main.
6. **Foster Drive – Government Street (Phase A):** This rehabilitation project involves replacing and rehabilitating 629 manholes and improvements to 80,600 linear feet of gravity main.
7. **Nicholson Dr – Highland Rd – Perkins Rd (Phase A):** This capacity project involves upgrades to approximately 8,400 linear feet of forcemain, 3,400 linear feet of gravity main and the rehabilitation/replacement of 20 manholes.
8. **Citiplace/Essen Area – PS119 and Forcemain Improvements:** This capacity project involves replacing one pump station and upgrading approximately 8,100 linear feet of forcemain.
9. **South Blvd-St. Joseph St/25th St – N. Acadian Thruway:** This capacity improvement project involves upgrading approximately 18,360 linear feet of forcemain and 3,000 linear feet of gravity main.
10. **Foster Drive – Government Street (Phase B):** This rehabilitation project involves upgrading approximately 78,700 linear feet of gravity main.

11. Capitol Lake Dr – Gayosa St/25th St – N. Acadian Thruway:

This capacity improvement project involves upgrading approximately 19,320 linear feet of forcemain and 19,150 linear feet of gravity main.

12. Downtown Area – Pump Station Improvements: This capacity project involves upgrading three pump stations.

13. Bluebonnet Blvd – Jefferson Hwy Phase 1: This rehabilitation project involves rehabilitating approximately 54,200 linear feet of gravity main.

14. Kenilworth Blvd – Boone Drive: This rehabilitation project involves rehabilitating approximately 72,000 linear feet of gravity main and 1,159 manholes.

15. Sharp Road – Florida Blvd: This rehabilitation project involves rehabilitating approximately 274,475 linear feet of gravity main and 1,154 manholes.

16. Bluebonnet Blvd – Jefferson Hwy Phase 2: This rehabilitation project involves rehabilitating approximately 63,100 linear feet of gravity main.

17. Silverleaf Road – Ford Street: This rehabilitation project involves implementing upgrades to 115,200 linear feet of gravity main.

18. Multiple PS – Jefferson Hwy – Park Forest Drive: This capacity project involves upgrading six pump stations.

19. Brookstown Road – Evangeline Street (Phase 2): Phase 2 of this rehabilitation project involves rehabilitating approximately 84,000 linear feet of gravity main and 1,075 manholes.

20. Brookstown Road – Evangeline Street (Phase 1): This rehabilitation project involves rehabilitating approximately 161,000 linear feet of gravity main and 1,150 manholes.

21. Highland Road – Burbank Drive: This capacity project involves upgrading approximately 39,400 linear feet of forcemain.





22. Zachary Area Transmission Network (Phase 4):

Phase 4 of this capacity project will upgrade approximately 42,500 linear feet of forcemain.

23. Group Project 1A (Veterans Parkway – Gravity Mains):

This capacity project involves upgrading approximately 46,000 linear feet of gravity main.

24. Choctaw Storage and PS Facility: This WWTP project involves replacing three pump stations and implementing improvements to approximately 25,000 linear feet of forcemain.

25. SWWTP Wet Weather Improvements (Phase 1): Phase 1 will provide wet weather storage, influent pumping, and preliminary treatment at the SWWTP.

26. Central Consolidation – PS42 Forcemain – Phase A: This capacity project involves upgrading one pump station and approximately 32,000 linear feet of forcemain.

27. Perkins/Old Perkins Area – Booster PS 514 Improvements: This capacity improvement project involves upgrades to one booster pump station.

28. Zachary Area Transmission Network (Phase 1): Phase 1 will involve upgrading three pump stations.

29. Zachary Area Transmission Network (Phase 3): Phase 3 of this capacity project will improve approximately 27,000 linear feet of forcemain.

30. Staring Lane Forcemain (Phase 2 – Highland to Perkins): This capacity project involves upgrading approximately 12,363 linear feet of forcemain.

31. Emergency Generators Purchasing: This project involves purchasing generators at each of the pump stations in East Baton Rouge Parish to ensure continuity of service during power failures.

32. Emergency Generators Installation: This project involves installing generators at each of the pump stations in East Baton Rouge Parish to ensure continuity of service during power failures.

PROJECTS COMPLETED AND UNDER CONSTRUCTION

COMPLETED PROJECTS

UNDER CONSTRUCTION

Project Information				Project Components				Consultant/Contractor Information		Cost	Schedule			
#	Project Name	Project Type	DPW Project #	Number of Up-graded Pump Stations	Number of Replaced / Rehabilitated Manholes *	Linear Feet of Forcemain Improvements	Linear Feet of Gravity Main Improvements	Design Consultant	Construction Contractor	Construction Contract Amount	Project Start	Advertise for Construction Bid	Project End	
1	RMAP1 - Kleinpeter Area Upgrades	***	RMAP1	03-RMP-S14	1	-	2,000	-	Monroe & Corie	Allen & LeBlanc	\$324,024	2/1/2008	7/14/2008	5/8/2009
2	Jefferson Highway-Hoo Shoo Too Road	PDP	Rehab	07-AR-US-0049	-	553	-	DPW	Allen & LeBlanc	\$1,769,438	5/16/2007	6/27/2008	9/22/2009	
3	Gurney Road - Joor Road	PDP	Capacity	07-PS-BD-0017	1	-	14,475	-	Neel-Schaffer	Grady Crawford	\$1,543,734	1/18/2008	8/29/2008	10/2/2009
4	25 th Street - North Acadian Thruway	PDP	Capacity	09-GS-UF-0008	-	-	-	Hartman Engineering	(design only)	\$0	2/2/2009	3/5/2010	2/26/2010	
5	Staring Lane - Boone Drive	PDP	Rehab	08-AR-UF-0004	-	665	-	139,050	CSRS, Inc.	Grady Crawford	\$5,416,540	11/27/2007	1/23/2009	5/3/2010
6	Comite Drive - Foster Road (Phase 1)	PDP	Capacity	07-PS-BD-0019	3	-	12,080	-	Monroe & Corie	Hemphill Construction	\$1,923,522	3/3/2008	1/16/2009	7/2/2010
7	Staring Lane FM (PH I - Burbank to Highland)	PDP	Capacity	06-WC-CP-0036	-	-	2,260	-	Monroe & Corie	James Construction	\$4,615,500	1/11/2008	9/19/2008	7/2/2010
8	RMAP1 - PS136 Area Upgrades	***	RMAP1	99-RMP-S16	9	-	27,700	20,700	Sigma Consulting	Nottingham Construction	\$8,994,709	2/1/2008	10/26/2008	9/15/2010
9	NWWTP Odor Control	PDP	WWTP	07-WT-TP-0030	-	-	-	-	Env. Eng Svcs	SEMS, Inc.	\$5,363,052	6/29/2007	9/30/2009	11/19/2010
10	Foster Road - Hooper Road	PDP	Capacity	07-FM-BD-0046	-	-	26,200	-	PEC	Hemphill Construction	\$8,761,675	2/14/2008	1/9/2009	11/30/2010
11	Burbank Road - Gardere Lane	PDP	Rehab	08-AR-UF-0003	-	787	-	168,300	CSRS, Inc.	Allen & LeBlanc	\$6,126,533	5/16/2007	11/14/2008	1/3/2011
12	RMAP1 - Industriplex Area Upgrades	***	RMAP1	99-RMP-S08	6	-	4,000	-	Forte & Tablada	BRH Garver	\$10,018,093	3/10/2008	10/31/2008	1/31/2011
13	Comite Drive - Foster Road (Phase 2)	**	Capacity	02-CS-HC-0001	-	-	-	1,361	Monroe & Corie	JB James Construction	\$895,957	6/23/2008	6/27/2009	3/17/2011
14	Sullivan Rd/Lovett Rd/Wax Rd	PDP	Capacity	07-PS-BD-0018	3	-	4,200	2,100	Hartman Engineering	Don M. Barron Contractor	\$2,158,346	1/17/2008	1/16/2009	3/17/2011
15	SWWTP IAPs Combined	PDP	WWTP	08-TP-BD-0031	-	-	-	-	CDM, MWH, URS Corp.	Brasfield & Gorrie	\$27,363,571	11/6/2006	12/12/2008	5/27/2011
				23	2,005	92,915	331,511			\$85,274,694				
1	Elm Grove Garden Road - Harding Blvd	PDP	Rehab	09-AR-BD-0012	-	839	-	199,500	CSRS, Inc.	Allen & LeBlanc	\$12,989,271	10/1/2008	9/25/2009	6/13/2011
2	Scotland Avenue - Progress Road	PDP	Rehab	09-AR-BD-0011	-	300	-	208,000	CSRS, Inc.	Magnolia Construction	\$9,207,594	9/9/2008	9/25/2009	6/14/2011
3	Group Project 2 - Small Pump Stations	PDP	Capacity	08-PS-IF-0046	7	-	-	-	ABMB Eng.	Grady Crawford	\$3,475,914	3/10/2008	3/26/2010	8/16/2011
4	Oak Villa Blvd - Choctaw Street	PDP	Rehab	08-AR-UF-0005	-	990	245,000	-	CSRS, Inc.	Grady Crawford	\$8,997,370	4/14/2008	5/15/2009	9/7/2011
5	Highland Road - Buchanan Street	PDP	Capacity	08-GS-ST-0021	-	-	4,465	8,390	Burk-Kleinpeter / Justice & Huang (JV)	Gilmore & Sons Construction Co.	\$4,325,851	3/14/2008	4/23/2010	10/5/2011
6	Foster Drive - Government Street Phase A	PDP	Rehab	09-AR-BD-0015A	-	629	-	80,600	CSRS, Inc.	Grady Crawford	\$4,819,752	5/25/2009	6/25/2010	10/20/2011
7	Nicholson Dr - Highland Rd - Perkins Rd Phase A	PDP	Capacity	09-FM-MS-0047A	-	20	8,400	3,400	Buchart - Horn	Grady Crawford	\$2,591,613	6/29/2009	10/29/2010	10/29/2011
8	Citiplace/Essen Area - PS119 & Forcemain Improvements	PDP	Capacity	08-FM-UF-0024	1	-	8,100	-	GSA Consulting Engineers, Inc.	BRH Garver	\$2,801,503	2/25/2008	8/20/2010	1/3/2012
9	S. Blvd-St. Joseph St/25 th Street - North Acadian Thrw	PDP	Capacity	08-GS-ST-0018	-	-	18,360	3,000	Evans-Graves/Hartman Engineering	Reynolds, Inc.	\$17,965,049	3/27/2008	4/16/2010	1/12/2012
10	Foster Drive - Government Street Phase B	**	Rehab	09-AR-BD-0015B	-	-	-	78,700	CSRS, Inc.	Insituform Technologies	\$2,863,100	5/25/2009	9/17/2010	2/17/2012
11	Capitol Lake Drive-Gayosa St/25 th St - N. Acadian Thrw	PDP	Capacity	07-PS-BD-0048	-	-	19,320	19,150	Hartman Engineering/Sheard-Koykendall & Assoc.	Morgan Contracting, Inc. of FL	\$10,497,568	1/14/2008	6/18/2010	2/17/2012
12	Downtown Area - Pump Station Improvements	PDP	Capacity	08-PS-ST-0056/57	3	-	-	-	Shaw Environmental & Infrastructure, Inc.	Guy Hopkins Construction Co.	\$4,841,000	3/24/2008	9/3/2010	2/27/2012
13	Bluebonnet Blvd - Jefferson Hwy Phase 1	PDP	Rehab	10-AR-MS-0042	-	-	-	54,200	CSRS, Inc.	Allen & LeBlanc	\$3,848,872	2/8/2010	3/18/2011	3/20/2012
14	Kenilworth Blvd - Boone Drive	PDP	Rehab	09-AR-BD-0014	-	1,159	-	72,000	CSRS, Inc.	Allen & LeBlanc	\$5,168,129	3/26/2009	10/8/2010	4/4/2012
15	Sharp Road - Florida Blvd	PDP	Rehab	09-AR-BD-0013	-	1,154	-	274,475	CSRS, Inc.	Reynolds, Inc.	\$17,492,855	1/15/2009	4/16/2010	7/6/2012
16	Bluebonnet Blvd - Jefferson Hwy Phase 2	PDP	Rehab	10-AR-MS-0043	-	-	-	63,100	CSRS, Inc.	Reynolds, Inc.	\$4,482,869	3/23/2010	4/29/2011	8/21/2012
17	Silverleaf Road - Ford Street	PDP	Rehab	10-AR-BD-0041	-	-	-	115,200	CSRS, Inc.	John Plott Company	\$8,024,946	10/26/2009	1/28/2011	8/30/2012
18	Multiple PS - Jefferson Highway - Park Forest Drive	PDP	Capacity	09-PS-MS-0046	6	-	-	-	CSRS, Inc.	Grady Crawford	\$2,922,472	6/8/2009	3/25/2011	9/19/2012
19	Brookstown Road - Evangeline Street (Phase 2)	PDP	Rehab	10-AR-BD-0040	-	1,075	-	84,000	CSRS, Inc.	John Plott Company	\$5,467,640	10/8/2009	11/12/2010	11/8/2012
20	Brookstown Road - Evangeline Street (Phase 1)	PDP	Rehab	10-AR-BD-0039	-	1,150	-	161,000	CSRS, Inc.	Grady Crawford	\$10,309,180	7/10/2009	10/15/2010	12/14/2012
21	Highland Road - Burbank Drive	PDP	Capacity	08-FM-ST-0023	-	-	39,400	-	GOTECH, Inc.	RACON, Inc.	\$20,591,067	3/31/2008	10/29/2010	1/18/2013
22	Zachary Area Transmission Network - Phase 4	PDP	Capacity	10-FM-IF-0005	-	-	42,500	-	SJB/Owen & White	Wicker Construction	\$7,091,115	3/24/2008	8/27/2010	1/22/2013
23	Group Project 1A (Veterans Parkway - Gravity Mains)	PDP	Capacity	08-GS-UF-0053	-	-	-	46,000	URS Corp.	Texas Sterling Construction Co.	\$19,581,108	3/10/2008	10/29/2010	2/8/2013
24	Choctaw Storage and PS Facility	PDP	WWTP	09-PS-UF-0009	3	-	25,000	-	CDM	Brasfield & Gorrie	\$43,237,000	4/14/2008	10/22/2010	3/11/2013
25	SWWTP Wet Weather Improve (Phase I)	PDP	WWTP	08-TP-BD-0033	-	-	-	-	CDM	Brasfield & Gorrie	\$108,443,892	6/23/2008	3/26/2010	4/18/2013
26	Central Consolidation - PS42 FM (Phase A)	PDP	Capacity	09-FM-MS-036A	1	-	32,000	-	SJB/Owen & White	TBA	(bid opening 6/16)	11/7/2008	4/29/2011	5/20/2013
27	Perkins/Old Perkins Area - Booster PS514 Improvements	PDP	Capacity	09-PS-MS-0034	1	-	-	-	GEC	Wharton-Smith, Inc.	\$8,387,000	4/24/2009	4/8/2011	5/22/2013
28	Zachary Area Transmission Network (Phase 1)	PDP	Capacity	10-FM-IF-0004	3	-	-	-	SJB/Owen & White	Max Foote Construction	\$18,486,500	3/24/2008	8/20/2010	5/28/2013
29	Zachary Area Transmission Network (Phase 3)	PDP	Capacity	10-FM-IF-0004	-	-	27,000	-	SJB/Owen & White	Hemphill Construction	\$8,947,920	3/24/2008	10/15/2010	7/23/2013
30	Staring Lane FM (PH II - Highland to Perkins)	PDP	Capacity	-	-	-	12,363	-	Monroe & Corie	JB James Construction	\$9,892,090	4/4/2009	8/6/2010	7/30/2013
31	Emergency Generators Purchasing	***	Other	09-PS-BD-0037	-	-	-	-	N/A	ARCO	\$19,100,000	2009	6/18/2010	9/26/2013
32	Emergency Generators Installation	***	Other	09-PS-BD-0037	-	-	-	-	N/A	Grady Crawford	\$7,113,634	2010	-	2013
				25	7,316	481,908	1,470,715			\$413,963,873				

* All manholes are inspected in the project area. Only some are rehabilitated or replaced.
 ** These projects are included in the Program Delivery Plan (PDP), however are not shown as phases A/1 and B/2. During design, it was determined that these projects should be split into phases for better constructability.

*** These projects are not included in the PDP, however are either Remedial Measures Action Plan 1 projects (RMAP1) or are projects identified in the Wastewater Master Plan (not part of the EPA Consent Decree)

UNDER DESIGN

Project Information

Design Consultant

Cost

Schedule

#	Project Name	Project Type		DPW Project #	Design Consultant	Estimated Construction Value	Project Start	Advertise for Construction Bid	Project End
1	Staring Lane FM (Ph III - Perkins to PS58)	PDP	Capacity	06-WC-CP-0036	Monroe & Corie	\$9,550,000	4/30/2009	5/27/2011	5/16/2013
2	Acadian Thruway - Perkins Road	PDP	Rehab	10-AR-BD-0044	CSRS, Inc.	\$3,915,500	5/31/2010	6/3/2011	9/12/2012
3	Stanford Avenue - Morning Glory Road	PDP	Rehab	10-AR-BD-0045	CSRS, Inc.	\$6,876,000	6/25/2010	6/24/2011	11/2/2012
4	Zachary Area Transmission Network - Phase 2:	PDP	Capacity	10-FM-IF-0003	SJB/Owen & White	\$14,583,700	3/24/2008	6/24/2011	10/25/2013
5	Bayou Duplantier Area Sewer Upgrades	PDP	Capacity	09-GS-MS-0042	Neel-Schaffer	\$4,374,000	8/31/2009	7/15/2011	8/28/2013
6	Central Consolidation FM (2,3,5,7,10)	PDP	Capacity	09-FM-MS-0033	Shread-Kuyrkendall & Associates, Inc.	\$10,601,000	11/7/2008	7/15/2011	8/20/2013
7	Acadian Thruway - Claycut Road	PDP	Rehab	10-AR-BD-0046	CSRS, Inc.	\$7,449,000	8/2/2010	7/22/2011	10/30/2012
8	Group Project 1B (Veterans Parkway - PS and FM)	PDP	Capacity	08-PS-UF-0054	Evans-Graves / Burk Kleinpeter	\$19,309,000	3/10/2008	7/22/2011	1/24/2014
9	Government St - S. Acadian Thruway	PDP	Capacity	09-GS-MS-0043	GSA Consulting Engineers, Inc.	\$4,680,000	8/28/2009	7/29/2011	11/16/2012
10	Central Consolidated Pump Stations (2,3,4,5,6,7,10, 91)	PDP	Capacity	09-PS-MS-0035	Burk Kleinpeter / J/G	\$16,592,000	11/7/2008	7/29/2011	3/31/2014
11	Nicholson Dr - Highland Rd - Perkins Rd Phase B	**	Capacity	09-FM-MS-0047	Buchart - Horn	\$7,965,000	6/29/2009	8/5/2011	5/7/2012
12	SWWTP Wet Weather Improve (Ph 2)	PDP	WWTP	08-TP-BD-0055	MWH	\$107,219,000	10/1/2008	8/19/2011	12/31/2014
13	Central Pump Station - PS 42	PDP	Capacity	09-PS-UF-0003	MWH	\$6,695,070	10/21/2008	8/26/2011	11/8/2013
14	Central Consolidation- PS42 FM - Phase II	**	Capacity	09-FM-MS-036B	SJB/Owen & White	\$11,600,000	11/7/2008	9/9/2011	7/8/2013
15	Highland Road - Washington Street	PDP	Rehab	10-AR-MS-0022	CSRS, Inc.	\$8,022,000	10/13/2010	9/9/2011	12/28/2012
16	PS 58 Overflow Pump Station	PDP	Capacity	09-PS-UF-0001	GEC	\$15,750,000	1/5/2009	9/9/2011	2/21/2014
17	Multiple PS - Nicholson Dr - Brightside Dr	PDP	Capacity	09-PS-MS-0048	Arcadis U.S., Inc.	\$6,113,000	9/14/2009	9/16/2011	1/31/2014
18	Plank Road - Kleinpeter Road	PDP	Capacity	09-GS-UF-0028	Forte & Tablada	\$7,583,000	3/23/2009	10/28/2011	1/10/2014
19	O'Neal Lane Pipeline Projects - A	PDP	Capacity	10-FM-MS-0008A	URS Corp.	\$12,157,000	9/29/2009	11/11/2011	4/21/2014
20	O'Neal Lane Pipeline Projects - B	**	Capacity	10-FM-MS-0008B	URS Corp.	\$5,300,000	9/29/2009	11/11/2011	4/21/2014
21	Airline Highway - Goodwood Blvd Phase 1	PDP	Rehab	TBA	CSRS, Inc.	\$11,900,000	1/10/2011	11/11/2011	9/17/2013
22	Hooper Storage	PDP	WWTP	09-PS-UF-0007	TRC Engineers	\$19,115,000	1/19/2009	11/18/2011	12/24/2013
23	Airline Highway - Goodwood Blvd Phase 2	PDP	Rehab	TBA	CSRS, Inc.	\$11,900,000	3/10/2011	1/6/2012	11/18/2013
24	Airline Highway Pipeline Projects	PDP	Capacity	10-GS-MS-0007	ABMB Eng.	\$35,200,000	1/30/2009	1/13/2012	12/31/2014
25	Lovett Road - Greenwell Springs - A	PDP	Capacity	10-FM-MS-0049A	SJB/Owen & White	\$13,364,000	5/3/2010	6/15/2012	12/31/2014
26	Lovett Road - Greenwell Springs - B	**	Capacity	10-FM-MS-0049B	SJB/Owen & White	\$8,780,000	5/3/2010	6/15/2012	12/31/2014
27	Hooper Road Pump Station	PDP	Capacity	10-PS-MS-0048	Stanley	\$11,935,000	5/3/2010	7/6/2012	12/31/2014
28	O'Neal Lane Pump Stations - A	PDP	Capacity	10-PS-MS-0050	MWH	\$12,226,000	5/25/2010	7/13/2012	12/31/2014
29	O'Neal Lane Pump Stations - B	PDP	Capacity	10-PS-MS-0051	URS Corp.	\$9,800,000	5/25/2010	7/13/2012	12/31/2014
30	Multiple PS - Highland Rd - Kenilworth Parkway	PDP	Capacity	10-PS-MS-0009	AECOM	\$8,926,760	2/8/2010	10/5/2012	12/31/2014
31	Highland Road Pipeline Improvements - A	PDP	Capacity	11-ES-PW-0002A	Evans Graves	\$9,741,000	1/28/2011	10/26/2012	4/11/2014
32	Highland Road Pipeline Improvements - B	**	Capacity	11-ES-PW-0002B	Evans Graves	\$8,118,000	1/28/2011	10/26/2012	4/11/2014
33	Plank Road Pump Station Improvements	PDP	Capacity	11-PM-MS-0024	(selection 6/16/11)	\$9,300,000	4/13/2011	12/7/2012	11/25/2014
34	Florida Blvd Pump Station Improvements	PDP	Capacity	11-PS-MS-0003	Brown & Caldwell	\$15,000,000	1/28/2011	12/28/2012	12/31/2014
35	Multiple PS - Burbank Drive - Siegen Lane	PDP	Capacity	11-PS-MS-0026	(selection 6/16/11)	\$4,100,000	5/2/2011	1/18/2013	12/31/2014
36	Oak Villa Blvd - Monterey Blvd	PDP	Capacity	11-FM-MS-0025	(selection 6/16/11)	\$9,000,000	4/18/2011	4/12/2013	12/31/2014
37	Joor Road - Greenwell Springs Road	PDP	Capacity	11-FM-MS-0023	(selection 6/16/11)	\$6,900,000	4/18/2011	4/22/2013	12/31/2014
38	Multiple PS - Highway 61 - Plank Road	PDP	Capacity	TBA	(will advertise 08/2011)	\$6,000,000	8/5/2011	5/3/2013	12/31/2014
39	Multiple PS - Prescott Rd - Greenwell Springs Rd	PDP	Capacity	TBA	(will advertise 08/2011)	\$4,800,000	8/5/2011	5/3/2013	12/31/2014
40	Plank Road - Port Hudson Pride Road	PDP	Capacity	TBA	(will advertise 08/2011)	\$4,800,000	8/5/2011	5/10/2013	12/31/2014
41	Sherwood Forest Blvd - Goodwood Blvd Pipeline Improve.	PDP	Capacity	11-FM-MS-0005	Forte & Tablada	\$10,200,000	1/3/2011	6/7/2013	12/31/2014

\$517,440,030

** These projects are included in the Program Delivery Plan (PDP), however are not shown as phases A and B. During design, it was determined that these projects should be split into phases for better constructability.

LOOKING AHEAD...

Projects Recently Advertised for Construction Bids

Central Consolidation Pump Station 42 Forcemain Capacity Improvement Project Phase A.

Estimated Construction Cost - \$16,610,000. Advertised April 29, 2011; Mandatory Pre-Bid Meeting May 18, 2011; Construction Bids due June 30, 2011.

Staring Lane Sewer Improvements Phase III (Perkins Road to Pump Station 058)

Estimated Construction Cost - \$8,390,000. Advertised May 27, 2011; Mandatory Pre-Bid Meeting June 14, 2011; Construction Bids due June 28, 2011.

Projects to be Advertised for Engineering Selection:

Plank Road Pump Station Capacity Improvement Project

Estimated Construction Cost - \$9,300,000. This project involves replacing nine pump stations in the North Gravity Basin to alleviate chronic SSOs at and near the pump stations. Advertised May 19, 2011; RFQs due June 2, 2011; selection June 16, 2011.

Multiple Pump Stations – Burbank Drive – Siegen Lane Capacity Improvement Project

Estimated Construction Cost - \$4,100,000. The project involves replacing six pump stations. The new pump stations will work in conjunction with the forcemain upgrades in other South Basin projects to alleviate chronic SSOs at and near these pump stations. Advertised May 19, 2011; RFQs due June 2, 2011; selection June 16, 2011.

Oak Villa Blvd – Monterey Blvd Capacity Improvement Project

Estimated Construction Cost - \$9,000,000. This project involves upsizing approximately 17,000 linear feet of gravity sewer pipe and approximately 1,000 linear feet of forcemain sewer pipe. Advertised May 19, 2011; RFQs due June 2, 2011; selection June 16, 2011.

Joor Road – Greenwell Springs Capacity Improvement Project

Estimated Construction Cost - \$6,900,000. This project involves upsizing approximately 5,600 linear feet of gravity sewer pipe and approximately 30,000 linear feet of forcemain sewer pipe. Advertised May 19, 2011; RFQs due June 2, 2011; selection June 16, 2011.

Projects to be Advertised for Construction Bids:

The following projects are expected to advertise for construction bid in June 2011:

- Acadian Thruway – Perkins Road Comprehensive Rehabilitation Project
- Stanford Avenue – Morning Glory Comprehensive Rehabilitation Project
- Zachary Area Transmission Network – Phase 2 Capacity Improvement Project

For more information, please visit the project website at www.brprojects.com

BATON ROUGE SSO PROGRAM PROGRESS REPORT

MAY 2011

300 North Boulevard, Room 208
Baton Rouge, LA 70802
(225) 389-3158
DPW@brgov.com

BATON ROUGE SSO
Program

